

## 2008 BOND

### CONSTRUCTION PROGRESS REPORTS

July 29, 2010

#### ORR ELEMENTARY SCHOOL

##### DENSON

New building is complete only minor punch list items remaining. Building is ready for occupancy.


Demolition of old campus is complete.

Work on parking areas is progressing well and will be complete prior to the start of school in August.

Concrete work is nearing completion in courtyard and landscaping is underway


The next month's progress will be the completion of Phase 2 sitework and landscaping.

A. W. ORR



FIRST FLOOR

NORTH KEY PLAN



SECOND FLOOR

NORTH KEY PLAN

**2008 BOND**  
**CONSTRUCTION PROGRESS REPORTS**  
**July 29, 2010**


**CLARKSTON ELEMENTARY SCHOOL**

**RPR**


Final Report.

This project has been completed under budget  
and over 4 months ahead of schedule.

CLARKSTON



 NORTH KEY PLAN



 NORTH SECOND FLOOR KEY PLAN

## 2008 BOND

### CONSTRUCTION PROGRESS REPORTS

July 29, 2010

#### WOODS ELEMENTARY SCHOOL

##### DENSON

Phase 1 work is complete and building is ready for occupancy.


Demolition of old campus is complete.

Work is underway on Phase 2 retaining walls, site fill and grading and installation of teacher's parking lot.


Concrete work is nearing completion in courtyard and landscaping is underway.

The next month's progress will be the continuation of all work in Phase 2 and the completion of the courtyard.

ANDY WOODS



← NORTH  
FIRST FLOOR  
KEY PLAN



← NORTH  
SECOND FLOOR  
KEY PLAN

**2008 BOND**  
**CONSTRUCTION PROGRESS REPORTS**  
**July 29, 2010**

**JONES/BOSHEARS SCHOOL**

**DENSON**

Final punch lists have been made on all areas.



Furniture and equipment was moved from St. Louis into the new Boshears on July 21<sup>st</sup> & 22<sup>nd</sup>.

Site grading is complete and landscaping is underway.

Correction of punch list items is nearing completion.

The next month's progress will be the completion of all buildings punch list work and detailing out the site work.

Jones - Boshears Elementary School

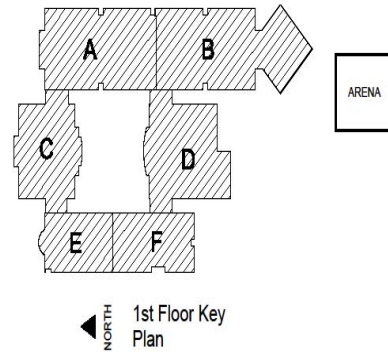

## 2008 BOND

### CONSTRUCTION PROGRESS REPORTS

July, 29, 2010

#### GRIFFIN ELEMENTARY

##### DENSON

Interior finishes are being installed in all areas of the 2 story building..

Parking lot is being graded and prepared for placing of concrete pavement..


Interior masonry is complete in gym and cafeteria.

Exterior brickwork on building is nearing completion.

Roofing at gym and cafeteria is complete


Work is starting on last remaining retaining walls.

Next months progress will be the continuation of all items listed above.



LOWER FLOOR

NORTH KEY PLAN



UPPER FLOOR

NORTH KEY PLAN

**2008 BOND**

**CONSTRUCTION PROGRESS REPORTS**

**July, 29, 2010**

**Birdwell Elementary**

**RPR Construction**

Concrete is being placed at new parking lot

Demolition work for 1<sup>st</sup> phase of remodeling is complete and renovations are underway.

Earthwork is complete in area of new addition and foundation work is ready to start.

Exterior work at new entrances is underway.

Site retaining walls are being constructed.

Next months progress will be completion of renovations at 1<sup>st</sup> phase of remodeling and installation of foundations for new additions

## **2008 BOND**

### **CONSTRUCTION PROGRESS REPORTS**

**July, 29, 2010**

#### **Owens Elementary**

##### **RPR Construction**

Interior demolition is complete for 1<sup>st</sup> phase of remodel work.

New parking lot at front of building is complete.

Foundation work at new classroom addition is complete and foundation work at new gym and cafeteria is started.

Interior finishes are being installed at 1<sup>st</sup> phase of the classroom areas.

The next months progress will be the completion of Phase 1 remodel work, foundations at gym and cafeteria and pouring of slab at new classroom addition.
