

2008 BOND
CONSTRUCTION PROGRESS REPORTS
August 23, 2010

ORR ELEMENTARY SCHOOL

DENSON

New building is set up and ready for school to start

Courtyard area is complete


New parking lots are complete.

Concrete play court is being installed


Ribbon Cutting August 22, 2010

The next month's progress will be the continuation of Phase 2 landscaping and overall project completion.

A. W. ORR



FIRST FLOOR
NORTH KEY PLAN



SECOND FLOOR
NORTH KEY PLAN

2008 BOND

CONSTRUCTION PROGRESS REPORTS

August 23, 2010

WOODS ELEMENTARY SCHOOL

DENSON

Phase 1 work is complete and building is ready for school to start.

Exterior concrete work and site grading is complete


Retaining walls are complete.

Courtyard area is complete.


Ribbon Cutting August 15, 2010

The next month's progress will be the completion of landscaping and fencing of the site.

ANDY WOODS



← NORTH
FIRST FLOOR
KEY PLAN



← NORTH
SECOND FLOOR
KEY PLAN

2008 BOND
CONSTRUCTION PROGRESS REPORTS

August 23, 2010

JONES/BOSHEARS SCHOOL

DENSON



Building is complete and set up and ready for school to start.

Punch list work on the site is nearing completion.

Ribbon Cutting August 22, 2010

The next month's progress will be the completion of the project.

Jones - Boshears Elementary School

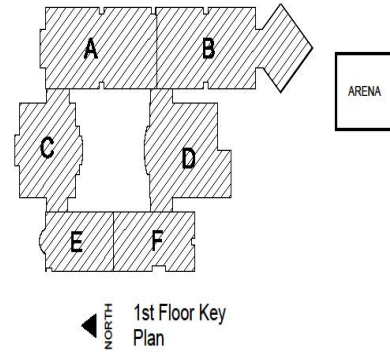

2008 BOND

CONSTRUCTION PROGRESS REPORTS

August, 23, 2010

GRIFFIN ELEMENTARY

DENSON

Interior finishes are being installed in all areas of the 2 story building.

North Parking Lot has been poured


West parking lot is being graded and prepared for placing of concrete pavement.

Brickwork on the building exterior is complete.



Finishes have started in the Gym and Cafeteria Areas.

Site grading has started


Next months progress will be the continuation of all items listed above.



LOWER FLOOR



UPPER FLOOR



2008 BOND
CONSTRUCTION PROGRESS REPORTS

August, 23, 2010

Birdwell Elementary

RPR Construction

New parking lot is complete and work is progressing on new entry for the building

Remodeling of 21 classrooms and associated corridors has been completed.

The new administration area is 50% complete and will be complete in early October.

Seats have been removed from existing Auditorium and are being refurbished.

Foundations for the new Gym, Cafeteria and Classroom addition is progressing well.

Next months progress will be continuation of work on the new Administration Area, completion of foundations for the new addition and completion of the new main entry to the building.

2008 BOND
CONSTRUCTION PROGRESS REPORTS

August, 23, 2010

Owens Elementary

RPR Construction

26 classrooms and associated corridors have been remodeled and are ready for classes to start.

A new connecting corridor has been constructed that ties what was a remote building to the rest of the campus.

Concrete slab has been placed and load bearing masonry walls at the new classroom addition are being installed.

Foundation work at the new Gym and Cafeteria is continuing.

Landscaping in at the new parking area is nearing completion.

The next months progress will be the completion of foundations at gym and cafeteria, completion of masonry walls at classroom addition and starting of remodeling of the existing Administration area.
