

2008 BOND

CONSTRUCTION PROGRESS REPORTS

June 17, 2010

ORR ELEMENTARY SCHOOL

DENSON

New furniture was delivered on 6-1-10.


Furniture and equipment from the existing campus was moved to the new building on June 5th & 6th.

Asbestos abatement and demolition is underway at old campus.

Concrete work is nearing completion in courtyard.


The next month's progress will be the completion of demolition of old campus, continuation of all work in Phase 2

A. W. ORR



FIRST FLOOR

NORTH KEY PLAN



SECOND FLOOR

NORTH KEY PLAN

2008 BOND

CONSTRUCTION PROGRESS REPORTS

June 17, 2010

CLARKSTON ELEMENTARY SCHOOL

RPR

Demolition of old campus is Complete.

New parking lot is complete.

Parking lot lighting is being installed


Sidewalks are complete.

Final grading of Phase 2 site is almost complete.


Landscaping has started on Phase 2

Progress for next month will be the completion of the project.

CLARKSTON



 NORTH KEY PLAN



 SECOND FLOOR
NORTH KEY PLAN

2008 BOND

CONSTRUCTION PROGRESS REPORTS

June 17, 2010

WOODS ELEMENTARY SCHOOL

DENSON

New furniture was delivered on 6-1-10.


Furniture and equipment from the existing campus was moved to the new building on June 5th & 6th.

Asbestos abatement and demolition is underway at old campus.


Concrete work is nearing completion in courtyard.

The next month's progress will be the completion of demolition of old campus, continuation of all work in Phase 2

ANDY WOODS



▲ NORTH
FIRST FLOOR
KEY PLAN



▲ NORTH
SECOND FLOOR
KEY PLAN

2008 BOND

CONSTRUCTION PROGRESS REPORTS

June 17, 2010

JONES/BOSHEARS SCHOOL

DENSON

Final punch lists have been made on all interior areas.

New furniture has been delivered and installed in Jones, Administration and Cafeteria.



Furniture and equipment was moved from the existing Jones campus to the new building on June 7 & 8.

Final grading and placing of top soil is underway in all areas.

Food service equipment installation is complete.

The next month's progress will be the completion of all buildings and detailing out the site work.

Jones - Boshears Elementary School

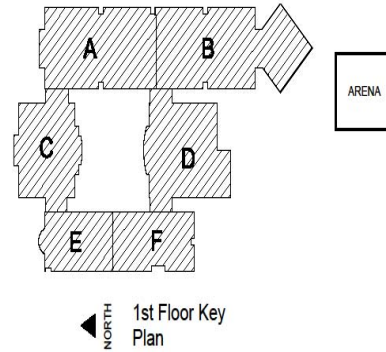

2008 BOND

CONSTRUCTION PROGRESS REPORTS

June, 17, 2010

GRIFFIN ELEMENTARY

DENSON

Interior and exterior drywall framing is complete in all classroom areas and sheetrock has been installed.

Ceiling grid and light fixtures are being installed in all classroom areas.

Steel erection is complete at gym and cafeteria and interior and exterior masonry is being installed.



Exterior brickwork is progressing well at 2 story classroom buildings.

Roofing is being installed at gym and cafeteria

Roofing installation at classroom wings is complete.

Most site retaining walls are complete.

Next months progress will be the continuation of all items listed above.



2008 BOND

CONSTRUCTION PROGRESS REPORTS

June, 17, 2010

Birdwell Elementary and Owens Elementary

RPR Construction

Contractor has mobilized on both sites

Furniture has been removed from the areas that will be renovated this summer.

Asbestos abatement is being done in preparation for starting demolition

The existing gym has been removed at Birdwell

Site demolition has begun at both sites in preparation for starting work on the new additions.

Next months progress will be interior demolition, starting of interior finishes and foundations for the new additions
